

BOARD OF EDUCATION



- d. Living Wage Report (Verbal) (R. Weston) 7:35 PM
- e. COVID-19 Update (K. Hachlaf) 7:40 PM [12](#)
- 4. **General Announcements** 7:50 PM
Pink Shirt Day, February 23. Please wear your Pink Shirts at the February 22 Board meetings.
- 5. **New Business** 7:55 PM
 - a. BCPSEA Report Out (Trustee Russell)
- 6. **Old Business** 8:10 PM
- 7. **Question Period (15 Minutes)** 8:15 PM
Questions to the Chair on matters that arose during the meeting.
- 8. **Adjournment** 8:30 PM



PROJECT STATUS REPORT

Project	Project Name McBride Replacement	Project Description	Construction of new building and demolitio of existing	
---------	--	------------------------	--	--



PROJECT STATUS REPORT

Project Schedule

Highlight any important changes or risks to the project timelines

The General Contractor had been aiming for opening December 2021 or Challenges 2021. The availability and delivery of materials subsequent flooding early in November, the continued extreme weather and continued challenges from COVID have resulted in delay in project completion. The General Contractor is now aiming for turnover of the building to School District prior to Spring Break.

The following table provides further details regarding the project schedule.

Task	Completed by	Status
Phase one newschool		Feb. 222

Se 284.69 1 fo1xce04.69 Excavation, shoring, micropiling, formwork for foundation



PROJECT STATUS REPORT

- additional requirements.
4. Post Completion Audit
 5. Escalation With the contractor placed this risk has been eliminated Change order pricing for required change potentially be impacted by the rising costs. Efforts continue to minimize change orders

Additional major risks include:


- f Safety construction vehicle access as well as construction site strategy to minimize danger to students and community. With classes underway the Superintendent and School Principal have been working together to ensure deliveries of materials do not impact arrivals and departures of students and ensure parents are not providing drop off via car on Archer Street. A potential issue of a building upon Archer Street near the storm drain was identified by the School Principal and the General Contractor agreed to make changes to their discharge to eliminate the risk.
- f Neighbours concerns regarding construction disruption. To date there have been few complaints and no substantial



PROJECT STATUS REPORT




Exterior Courtyard Progressing



Gym Floor Installed with Sanding ongoing



PROJECT STATUS REPORT

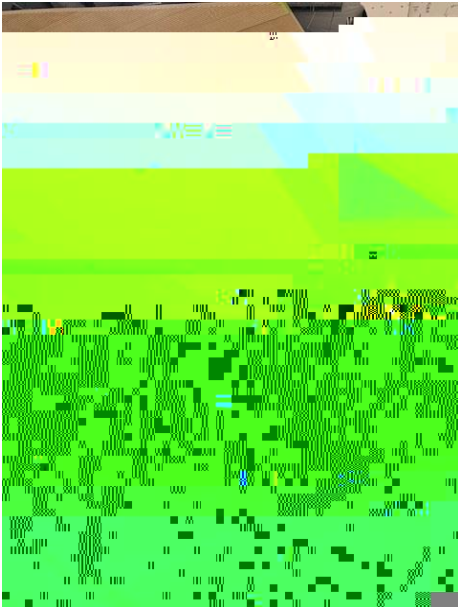

Wood Slat Ceiling



Classroom Millwork progressing



PROJECT STATUS REPORT



Collaborative Learning Space Millwork Installation



Operations Update

February 8, 2022

Capital Projects, Operations and Planning

1. The 64 HEPA filters purchased by the District in January have all been deployed to portables and certain school



Student and Staff Illness

Provincial K -12 Communicable Disease Guidelines
